



# WHS Life Complex Construction Update

October 2024



TACKarchitects



IMPACTING EXCELLENCE  
Celebrate the past. Support the future.




## WHS LIFE COMPLEX MILESTONES

MAR 4 '24  
MOBILIZE SOUTH PARKING



MAY-JUNE '24  
SITE UTILITIES



OCT '24-FEB '25  
PRECAST STRUCTURAL STEEL




NOV '25-MAR '26  
RENOVATION

MAR '26  
PROJECT COMPLETE

APR-MAY '24  
BUILDING DEMO



AUG-OCT '24  
FOUNDATIONS




OCT 31 '25  
POOL COMPLETE



## Construction Update October

Through the month of October & early November the building structure has started to take shape. The east and south foundation walls were completed to the extents required for structural install. A portion of the south wall will remain open to allow material and equipment access for pool installation. Structural steel erection continued with the completion of NE Stair Tower, East Level 1 (locker rooms & classrooms), East Level 2 (training & therapy), and East Level 3 (pool seating and concourse). Construction of the pool structure began with completion of the west pool wall and surge tank walls. The first slab pour took place on 11/11 infilling the old pool. This slab will be the future fitness center/wrestling room.

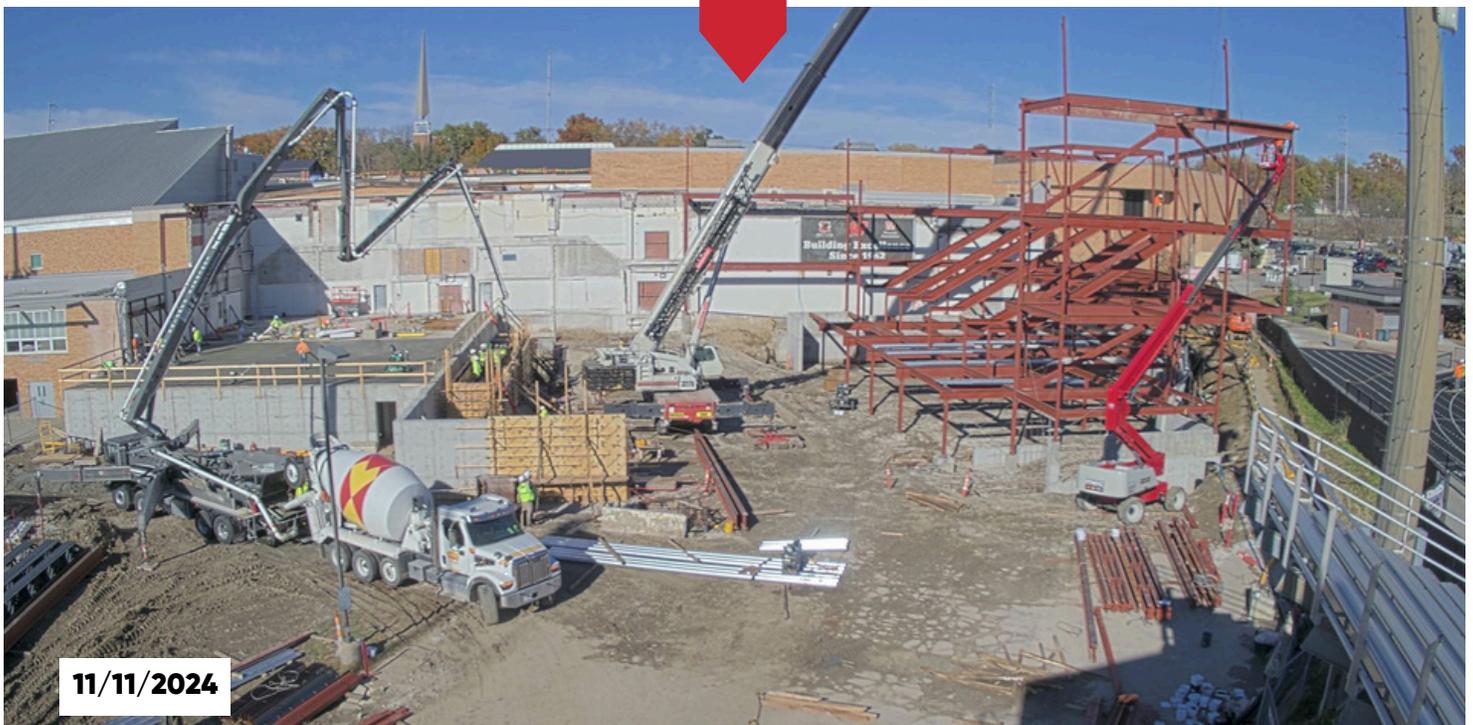



## Student Engagement

Weitz continues to meet with Westsides ACE (architecture, engineering, construction) program every 2 weeks. Recently the ACE group and (3) groups from the advanced welding class each toured the jobsite on 11/8/24.



Brock Johnson showing students 3D model of the project inside Weitz project trailer.



Welding Class tour viewing field assembly of the east truss.



**10/18/2024** Level 1 Structural Steel



**10/20/2024** Level 1 Structural Steel - Drone photo by  
WHS Student Elijah Bessmer



10/31/2024 Install of the signed beam




11/8/2024 Level 3 Structural Steel - Drone photo by  
WHS Student Elijah Bessmer



11/1/2024 Install of the signed beam




11/11/2024 Level 1 West Slab Pour

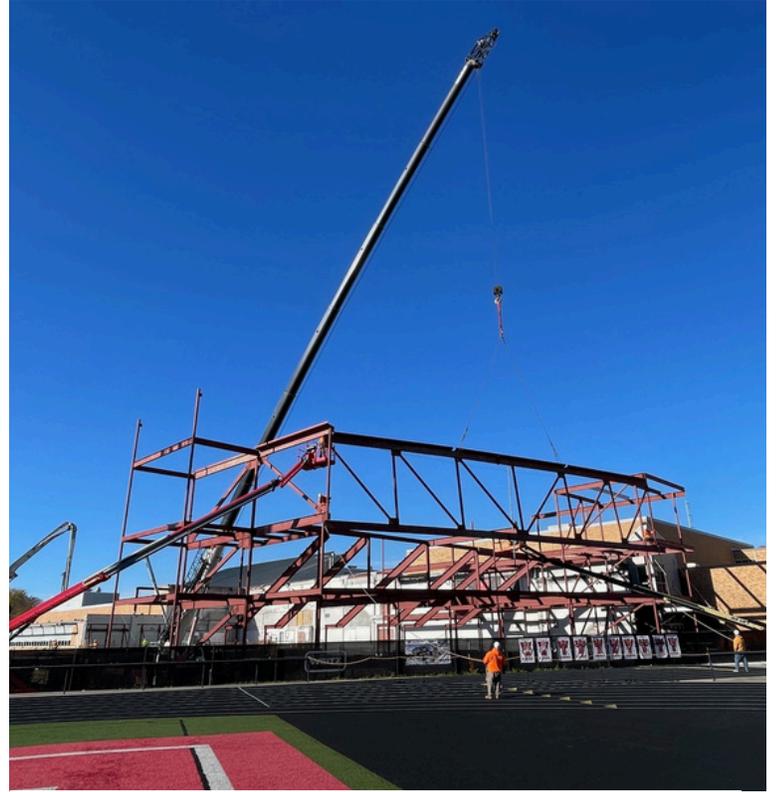

11/11/2024 Level 3 Structural Steel – East Truss  
*(This truss is 91' long x 19' tall and weighs 14,000 lbs. It was put together on the ground and lifted into place as one piece.)*



11/11/2024

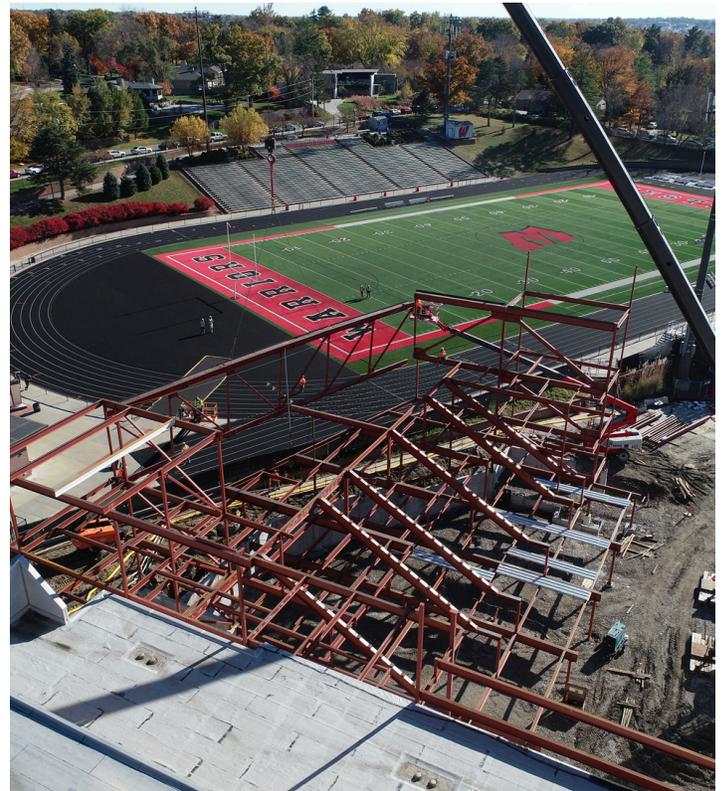

11/11/2024
