



WHS Life Complex Construction Update

January 2025



TACKarchitects



IMPACTING EXCELLENCE
Celebrate the past. Support the future.




WHS LIFE COMPLEX MILESTONES

MAR 4 '24
MOBILIZE SOUTH PARKING



MAY-JUNE '24
SITE UTILITIES



OCT '24-FEB '25
PRECAST STRUCTURAL STEEL




NOV '25-MAR '26
RENOVATION

MAR '26
PROJECT COMPLETE

APR-MAY '24
BUILDING DEMO



AUG-OCT '24
FOUNDATIONS



OCT 31 '25
POOL COMPLETE



Construction Update January

A lot of activity on the jobsite through the holidays and January. Our main focus was completing the steel structure, install precast stadia seating, and begin pouring the east elevated slabs. The pool walls and gutters continue to progress as we prepare for the arrival of the Myrtha pool package. Interior metal stud framing and cmu walls have started on Level 1 east which make up the locker rooms.


The ACE mentoring program is getting going again. Brock Johnson with Weitz meets with the ACE students each week to provide assistance with their projects.

12/12/2024



2/4/2025



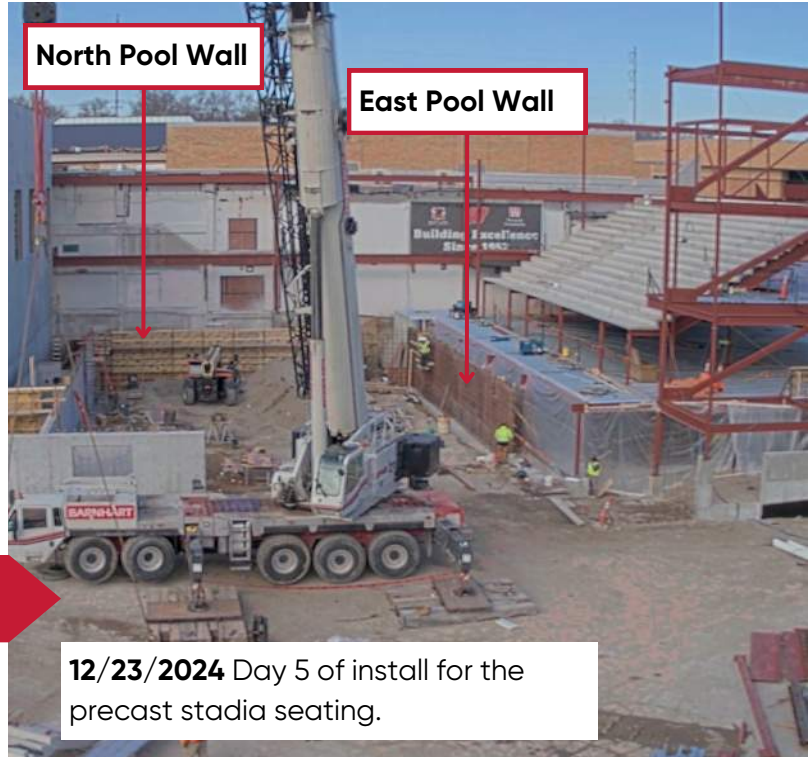

1/15/2025 Precast Panels Set on South Wall and Level 1 showers poured.



2/5/2025 Temp enclosure below level 3 and forming intermediate steps on the stadia seating.





TACKarchitects

